

**DIOCESE OF CHARLESTON  
BUILDING AND RENOVATION ADVISORY COMMITTEE  
MONTHLY PROJECT UPDATE REPORT**

**PARISH:** St Mary Magdalene Catholic Church

**DATE OF REPORT:** Nov 1, 2019

**PROJECT:** Parish Life Building

**CONTACT PERSON:** Deacon Roger Schonewald


**Please provide a brief summary of any accomplishments in regard to your building/renovation project during the previous month.**

At the end of October we were 6 weeks into the construction activities. During October;

1. The grading of the building pad was completed and the building pad was certified on Oct 10.
2. The building footings were poured on Oct 18.
3. Foundation masonry began on Oct 21 and was completed on Oct 30.
4. On Sunday, October 27 we held the official ground-breaking ceremony and site blessing presided over by our Bishop.



*(Building Foundation – Oct 28)*

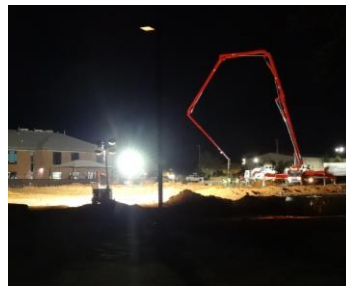

*(Pouring Footings – Oct 18)*



*(Ground Breaking with Bishop – Oct 27)*

**Any problems experienced in the past month? (If yes, please explain)**

No problems. Three “rain out” days during October. A few unexpected (and minor) changes covered by recently approved Change Order

**What are the project goals for the upcoming month?**

5. Pour the Fellowship Hall floor
6. Subsequent two flooring pours covering additional flooring areas of the building
7. Complete storm drain installation (provided weather stays dry enough)
8. Begin block walls

*Note: two live-stream cameras with time-lapse records of the construction site available from the parish website ... [smmcc.org/464](http://smmcc.org/464)*

**What is the estimated percentage of the project completion? 11%**

(PLEASE SEND TO YOUR REGIONAL PROJECT LIAISON AND STEPHANIE MCLELLAN VIA EMAIL, [smcclan@charlestondiocese.org](mailto:smcclan@charlestondiocese.org), NO LATER THAN THE 1<sup>st</sup> THURSDAY OF EACH MONTH. INCLUDE CURRENT PROJECT CASH FLOW REPORTS.)
